


## Sales Tax Bond Issue – Projects Update

### Jacksonville Cato – Capital Paving and Construction (CPC)

The Jacksonville Cato Project is gearing up. First, a reminder with the details of the project. Divided into two phases, phase I of the project starts at Lybrand Drive, just beyond CATO Elementary School, and continues for approximately 4,980 feet or 0.943 miles eastward. Once CPC begins, phase I is scheduled to run for 450 calendar days. Phase II will continue where Phase I ended and terminate at Highway 107. A twelve-foot (12') wide bike/ped path will flank the north side of the road, while a five-foot (5') wide sidewalk will be located on the south side.

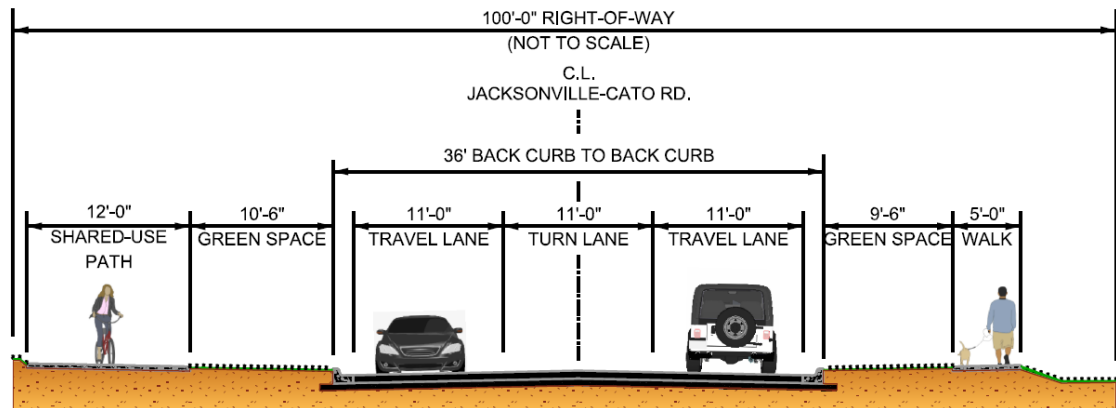

**TYPICAL SECTION**  
PROPOSED DESIGN PHASE 1

#### Phase I

The final two acquisitions in this phase have recently been secured. Central Arkansas Water has contracted to relocate the water main to Diamond Construction. After a lengthy supply chain delay, Diamond cleared the easement area on the south side of the trees and installed 90% of the water main. Two cuts have been made in the existing roadway, allowing for the placement of the water main for future development on the north side of Jacksonville CATO. First Electric Coop has cleared the easement area on the north side of the roadway and will begin pole relocations in the coming weeks. CPC started working on erosion control items, silt fencing, and rock check dams at the creek/bridge area by the school. ADEQ and Army Corps of Engineers permits are in place. The required wetland mitigation credits have been purchased at Pelican Mitigation LLC land bank.



Oct 11, 2023 9:19:22 AM  
9811 Jacksonville-Cato Road

Silt fence and rock check dams at creek/bridge city limit



Oct 10, 2023 9:49:24 AM  
9121 Jacksonville-Cato Road

Temporary Road allowing for street cut, water main installation



Oct 18, 2023 11:08:48 AM  
9121 Jacksonville-Cato Road

Staging NEW utility poles



Oct 18, 2023 12:26:44 PM  
9105 Jacksonville-Cato Road

7 NEW fire hydrants along NEW water main

## SUBSTANTIALLY COMPLETE:

### Hemphill Road – Redstone Construction Group

Major construction has been completed. Inspection has been performed and a punch list of items was forwarded to the contractor for correction.

## COMPLETED PROJECTS:

Maryland Avenue Widening (107 end) – Gene Summers Construction

Country Club Road – Weaver Bailey Contractors Inc.

Maryland Avenue Widening (Stonehill) – Burkhalter Technologies

Greenview Drainage – Cisneros Family Construction

Whitewood Drive Drainage – Redstone Construction Group
