

Sales Tax Bond Issue – Projects Update

Jacksonville Cato – Capital Paving and Construction (CPC)

Phase I

The Jacksonville Cato Project Phase I is progressing at full steam. We have weathered the rainy season with only modest delays to the schedule. Drainage pipe has been installed on the northside of the new roadway. Crews have been eagerly waiting for the last fiber cable to be relocated to the new utility poles. Once the cable is removed from the poles and the old poles removed installation can continue with the remaining drainage piping.

The Rodgers Group has been hard at work milling and leveling different areas where needed. They have also paved the DETOUR road over the new box culvert. Once the temporary barrier wall and striping are completed on Monday, June 24, there will be a lane shift to the detour road. With traffic on the new asphalt, the old box culvert will be removed and Mobley Contractors will complete the construction of the seven bay box culvert and pedestrian underpass.




On Detour Road over Bridge



Traffic Shift

TUESDAY, June 25, 2024


SLOW DOWN IN CONSTRUCTION ZONES!!!

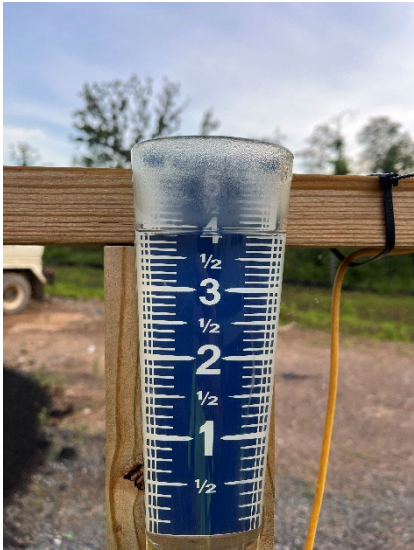

4" of rain 6-3-2024



First section of 7 bay box culvert and
pedestrian underpass

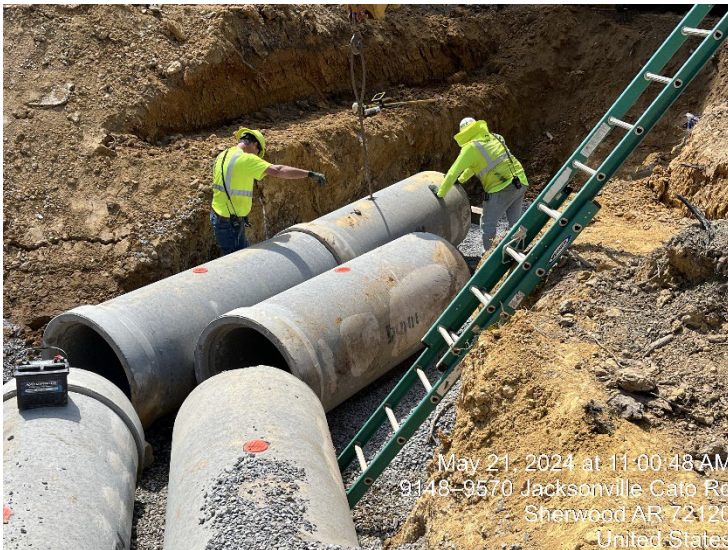

SLOW DOWN –
IN CONSTRUCTION ZONES



Drainage pipe @ location of junction box.

Crews working on Jacksonville Cato Road have a tough job. With temperatures approaching 100+, temps can be just as high. Please provide these crews with the SAFEST space you can, they want you to get to your destination with minimal delay.

They also want to make it home safely themselves.
